

[illegible]

Reb. Infr. rutiera DJ663, DJ672C,DJ672B,DJ665A, DJ664: actualizati la Februarie 2026 Update

CRITICAL_LAYOUT_FEB_2026

07-Mar-26 12:22

104

EX-663-90

Amplasare acces la punct

216

21-Jan-26

22-Feb-27

0%

26

RON181.77(10)

RON000

105

EX-663-110

Amplasare drum lateral

105

03-Nov-26

22-Feb-27

0%

25

RON222.25(6)

RON000

106

EX-663-90

Amplasare deal de cutare

112

13-Oct-26

02-Feb-27

0%

45

RON262.72(6)

RON000

107

EX-663-130

Amplasare intersectie cu DJ

45

28-Dec-26

11-Feb-27

0%

36

RON44.16(2)

RON000

108

EX-663-100

Amplasare trotuar la intrare cur

60

15-Nov-26

14-Jun-27

0%

65

RON107.60(3)

RON000

109

EX-663-120

Pavimentarea

60

16-Nov-26

14-Jun-27

0%

34

RON234.22(2)

RON000

110

EX-663-140

Semnalezica, marcaje si sigle

19

03-Feb-27

22-Feb-27

0%

27

RON182.85(3)

RON000

111

EX-663-160

Notificarea si efectuarea Rep.

60

23-Apr-27

24-Apr-27

0%

26

RON000

RON000

112

EX-663-100

Asistenta Proiectant Indirect

27

02-Mar-26

29-Mar-27

0%

35

RON000

RON000

113

EX-663-100

Asistenta Proiectant Indirect

27

20-Feb-26

20-Feb-27

0%

35

RON000

RON000

114

EX-663-100

Organizarea Seder DUBO

221

02-Feb-27

22-Feb-27

0%

39

RON105.76(4)

RON000

115

Dumrul Lateral

60

09-Nov-26

22-Feb-27

19

RON000

RON000

116

EX-663-160

Sapatura

6

09-Nov-26

17-Nov-26

0%

19

RON000

RON000

117

EX-663-170

Strat formaleasp - 10cm dupa

10

23-Jan-27

10-Jun-27

0%

19

RON000

RON000

118

EX-663-260

Fundatie balast - 30cm dupa

10

12-Jan-27

26-Jan-27

0%

19

RON000

RON000

119

EX-663-260

Plata Sparta - 20cm dupa compactare

7

26-Jan-27

04-Feb-27

0%

19

RON000

RON000

120

EX-663-300

Amplasare PS, curentului

2

04-Feb-27

09-Feb-27

0%

19

RON000

RON000

121

EX-663-310

BAD Z24 - 6cm incluzand paze

2

09-Feb-27

10-Feb-27

0%

19

RON000

RON000

122

EX-663-320

Amplasare BAD Z24 curentului

2

10-Feb-27

12-Feb-27

0%

19

RON000

RON000

123

EX-663-330

BA 18 sau BAR 18 - 4cm

2

12-Feb-27

16-Feb-27

0%

19

RON000

RON000

124

EX-663-340

Acostament Plata Sparta - 1%

4

16-Feb-27

22-Feb-27

0%

19

RON000

RON000

125

EX-663-300

Domeniu post-electrictate m

3

17-Nov-26

20-Nov-26

0%

19

RON000

RON000

126

EX-663-320

Montare si montajare la DF

2

03-Dec-26

10-Dec-26

0%

19

RON000

RON000

127

EX-663-260

Asistenta material dintr-un punct

2

16-Dec-26

16-Dec-26

0%

19

RON000

RON000

128

EX-663-210

Fundatie post

6

20-Nov-26

02-Dec-26

0%

19

RON000

RON000

129

EX-663-260

Montare si montajare la DF

3

11-Dec-26

16-Dec-26

0%

19

RON000

RON000

130

EX-663-220

Realizare sigla de intrare pe post

3

03-Dec-26

10-Dec-26

0%

19

RON000

RON000

131

EX-663-260

Hidrosculele post

3

16-Dec-26

23-Dec-26

0%

19

RON000

RON000

132

Proiectia Modulului si Asistenta Tehnica la Starea Tehnica

90

16-Nov-26

14-Feb-27

34

RON000

RON000

133

EX-663-100

Siguranza de incalzire

10

16-Nov-26

14-Feb-27

34

RON000

RON000

134

EX-663-140

Marci culer (marci reflector)

15

03-Feb-27

27-Feb-27

27

RON126.16(4)

RON000

135

EX-663-410

Longitudinala (15 cm latime)

14

03-Feb-27

17-Feb-27

27

RON000

RON000

136

EX-663-400

Transversala (15 cm latime)

5

17-Feb-27

22-Feb-27

27

RON000

RON000

137

EX-663-440

Indicatore de circulatie

10

09-Feb-27

28-Feb-27

27

RON000

RON000

138

EX-663-400

Indicatore de circulatie (diagonal)

5

09-Feb-27

21-Feb-27

28

RON000

RON000

139

EX-663-300

Stapa din beton de indicatie

15

03-Feb-27

19-Feb-27

28

RON000

RON000

140

EX-663-370

Borometru

10

08-Feb-27

18-Feb-27

31

RON000

RON000

141

EX-663-300

Borometru

10

08-Feb-27

18-Feb-27

31

RON000

RON000

142

EX-663-380

Stapa din beton de indicatie

10

08-Feb-27

18-Feb-27

31

RON000

RON000

143

EX-663-430

Panopie metalic tip H2

18

03-Feb-27

21-Feb-27

28

RON000

RON000

144

EX-663-401

ZID DE SPRIND DIN BETO

100

07-Apr-26

15-Jul-26

68

RON655.56(6)

RON000

145

EX-663-402

Fundatie adancita de pompet

100

07-Apr-26

15-Jul-26

68

RON1055.17(4)

RON000

146

Interventia DUBO la CNB

30

26-Dec-26

11-Feb-27

25

RON000

RON000

147

EX-663-520

MAS 18 - 4cm

2

05-Feb-27

09-Feb-27

26

RON000

RON000

148

EX-663-510

BAD Z24 - 6cm

2

05-Feb-27

09-Feb-27

26

RON000

RON000

149

EX-663-480

AB Z15 - 6cm incluzand paze

8

23-Jan-27

26-Jan-27

26

RON000

RON000

150

EX-663-480

Plata Sparta - 20cm dupa compactare

8

23-Jan-27

26-Jan-27

26

RON000

RON000

151

EX-663-470

Fundatie balast - 30cm dupa

8

23-Jan-27

26-Jan-27

26

RON000

RON000

152

EX-663-480

Strat formaleasp - 10cm dupa

8

26-Dec-26

10-Jan-27

26

RON000

RON000

153

EX-663-500

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

154

EX-663-500

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

155

EX-663-500

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

156

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

157

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

158

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

159

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

160

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

161

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

162

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

163

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

164

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

165

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

166

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

167

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

168

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

169

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

170

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

171

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

172

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

173

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

174

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

175

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

176

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

177

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

178

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

179

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

180

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

181

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

182

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

183

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

184

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

185

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

186

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

187

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

188

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

189

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

190

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

191

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

192

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

193

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

194

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

195

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

196

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

197

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

198

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

199

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

200

EX-663-510

Amplasare PS + AB Z15+B

2

03-Feb-27

05-Feb-27

26

RON000

RON000

Actual Work

Remaining Work

Summary

Activities

Milestone

Page 2 of 36

TASK filter: All Activities

© Oracle Corporation

[illegible]

Reab. Infr. rutiera DJ663, DJ672C, DJ672B, DJ665A, DJ664: actualizat la Februarie 2026 Update

CRITICAL_LAYOUT_FEB_2026

07-Mar-26 12:22

Legend:

- Actual Work
- Remaining Work
- Summary

TASK filter: All Activities

© Oracle Corporation

© Oracle Corporation

[illegible]

© Oracle Corporation

[illegible]

[illegible]

Activities
Remaining Work
Summary
Page 11 of 36
TASK filter: All Activities
© Oracle Corporation

© Oracle Corporation

© Oracle Corporation

Activities
Remaining Work
Summary
Page 14 of 36
TASK filter: All Activities
© Oracle Corporation

Activities
 Remaining Work
 Summary

Actual Work


 Milestone

Page 17 of 36
 TASK filter: All Activities

© Oracle Corporation

■ Activities ■ Remaining Work ▶ Summary Page 20 of 36 TASK filter: All Activities © Oracle Corporation

[illegible]

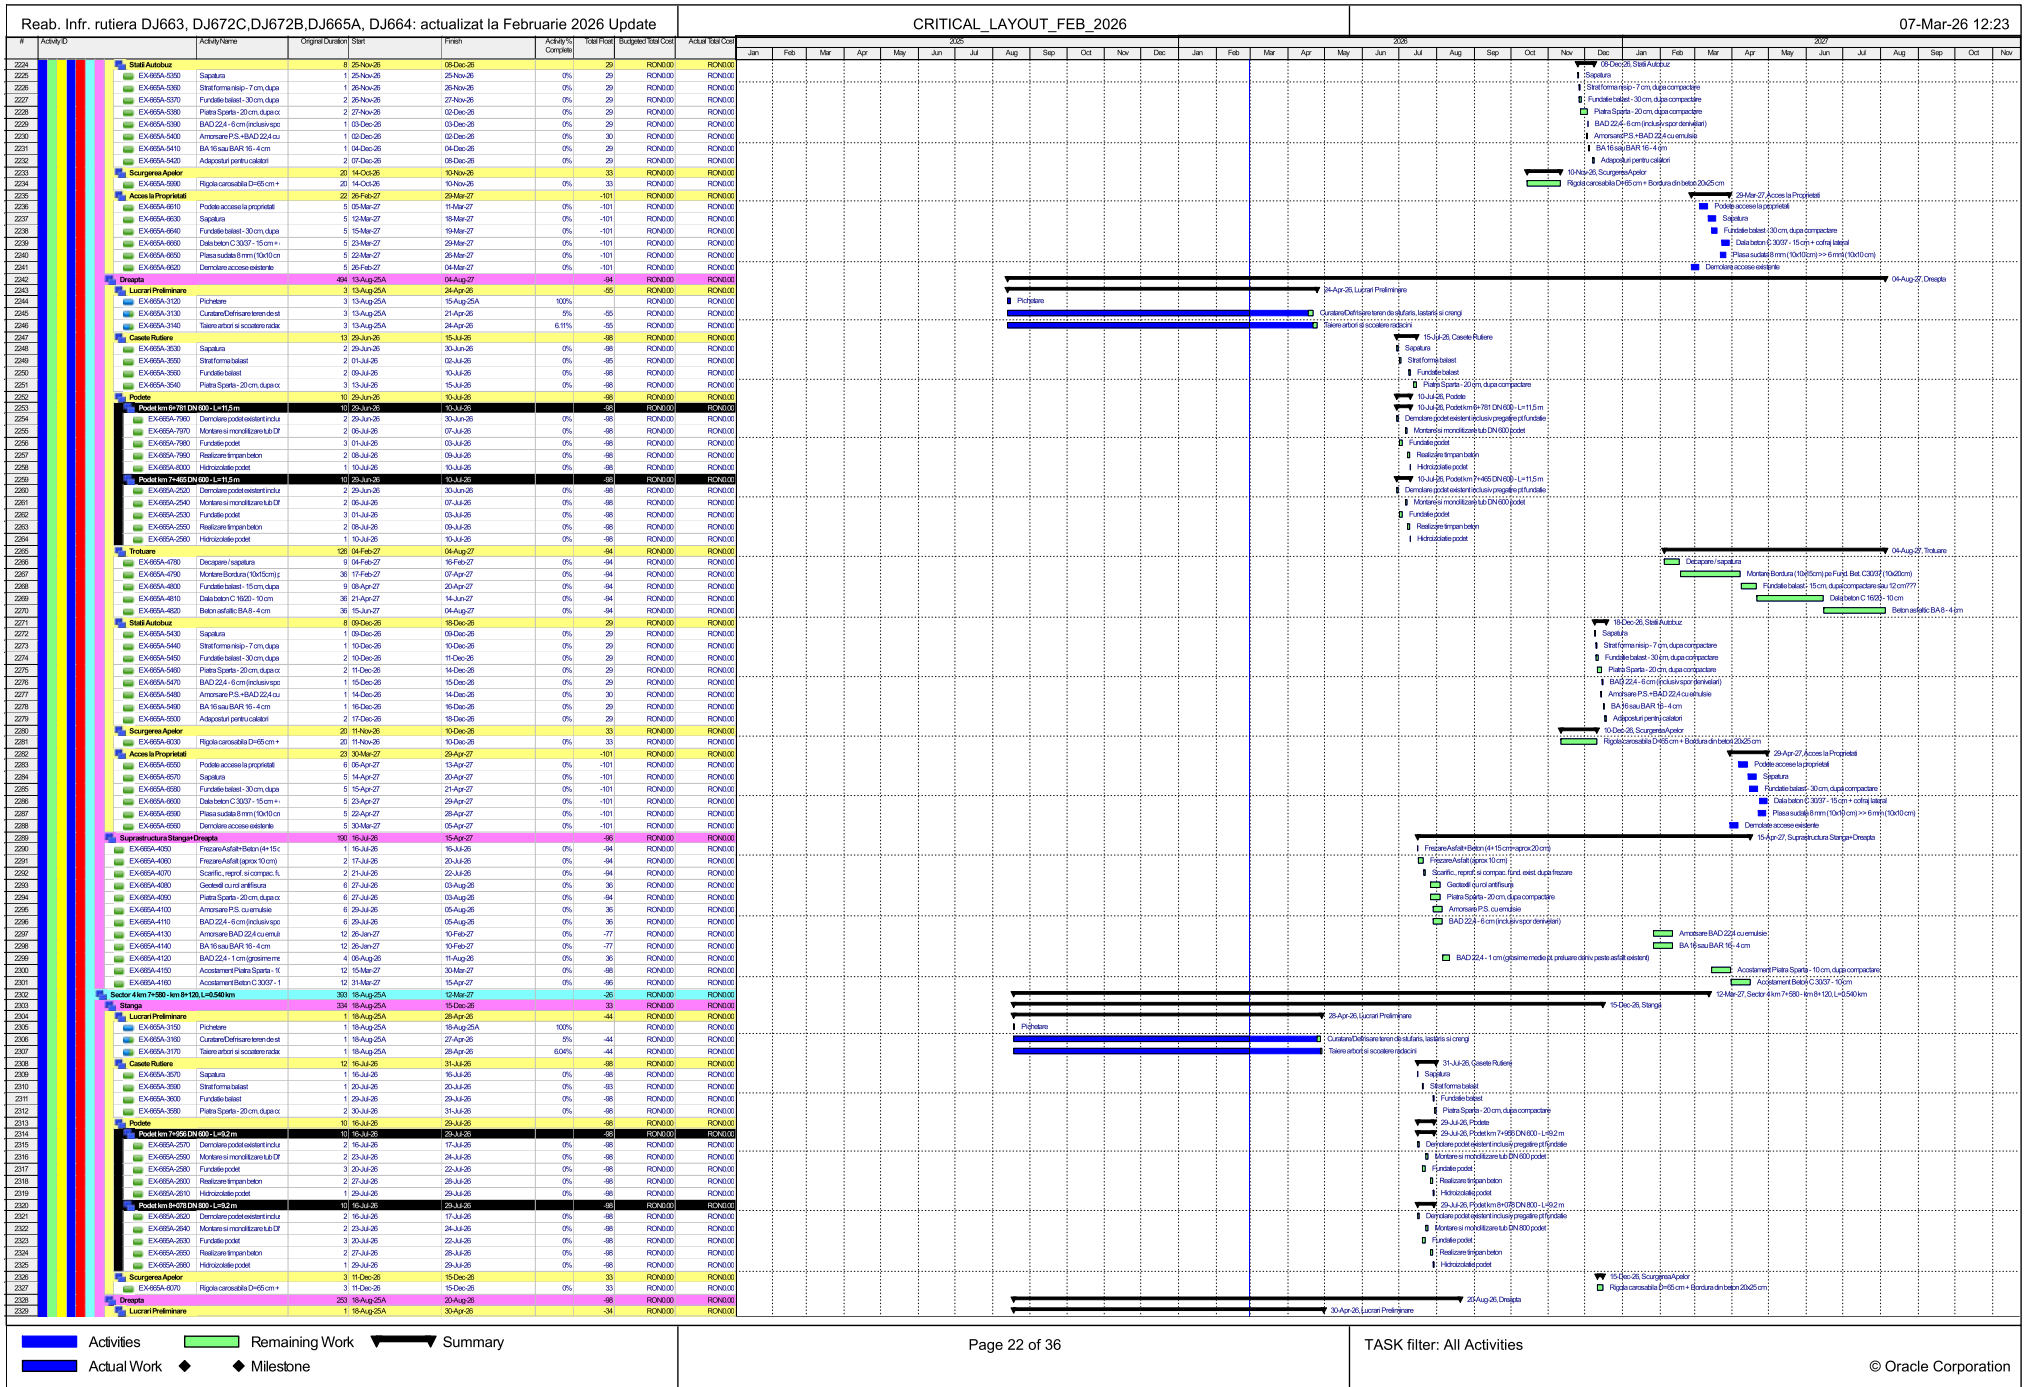

■ Activities ■ Remaining Work ➡ Summary

■ Actual Work ◆ Milestone

Page 23 of 36

TASK filter: All Activities

© Oracle Corporation

■ Activities ■ Remaining Work ➡ Summary
■ Actual Work ◆ Milestone

Page 24 of 36

TASK filter: All Activities

© Oracle Corporation

Reb. Infr. rutiera DJ663, DJ672C, DJ672B, DJ665A, DJ664: actualizat la Februarie 2026 Update

CRITICAL LAYOUT FEB 2026

07-Mar-26 12:23

Activities Remaining Work Summary

Actual Work Milestone

TASK filter: All Activities

Page 25 of 36

© Oracle Corporation

[illegible]

Reab. Infr. rutiera DJ663, DJ672C, DJ672B, DJ656A, DJ664: actualizat la Februarie 2026 Update

CRITICAL_LAYOUT_FEB_2026

07-Mar-26 12:23

Task List (Left):

- 2763 EX4672B-7200 Picturare 05-Jan-26 26-Apr-26 42 RONGUI RONGUI
- 2764 EX4672B-7200 Conturări Definiție linie de stat. 10-Mar-26 27-May-26 42 RONGUI RONGUI
- 2765 EX4672B-7200 Supliment 10-Mar-26 27-May-26 42 RONGUI RONGUI
- 2766 EX4672B-7200 Stratobază 10-Mar-26 27-May-26 42 RONGUI RONGUI
- 2767 EX4672B-7200 Strat. Pista Sport 10-Jun-26 25-Jun-26 42 RONGUI RONGUI
- 2768 EX4672B-7200 Instalare semnalizare de drum 11-Jun-26 25-Jun-26 42 RONGUI RONGUI
- 2769 EX4672B-7200 Instalare post tempor 30-Jun-26 11-Aug-26 42 RONGUI RONGUI
- 2770 EX4672B-7500 Decalcare post tempor 30-Feb-27 05-Apr-27 42 RONGUI RONGUI
- 2771 EX4672B-7300 Decalcare semnalizare de drum 26-Apr-27 07-Apr-27 42 RONGUI RONGUI
- 2772 EX4672B-7300 Decalcare semnalizare de drum 15-Aug-26 01-Sep-26 42 RONGUI RONGUI
- 2773 EX4672B-7300 Demontare post semnalizare de drum 15-Aug-26 01-Sep-26 42 RONGUI RONGUI
- 2774 EX4672B-7300 Fundatie pod 30-Sep-26 13-Oct-26 42 RONGUI RONGUI
- 2775 EX4672B-7300 Fundatie Culei 1 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2776 EX4672B-7300 Fundatie podului 5-225-culei 1 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2777 EX4672B-7300 Fundatie Culei 2 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2778 EX4672B-7300 Fundatie podului 5-225-culei 2 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2779 EX4672B-7300 Fundatie Culei 3 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2780 EX4672B-7300 Fundatie podului 5-225-culei 3 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2781 EX4672B-7300 Fundatie Culei 4 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2782 EX4672B-7300 Fundatie podului 5-225-culei 4 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2783 EX4672B-7300 Fundatie Culei 5 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2784 EX4672B-7300 Fundatie podului 5-225-culei 5 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2785 EX4672B-7300 Fundatie Culei 6 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2786 EX4672B-7300 Fundatie podului 5-225-culei 6 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2787 EX4672B-7300 Fundatie Culei 7 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2788 EX4672B-7300 Fundatie podului 5-225-culei 7 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2789 EX4672B-7300 Fundatie Culei 8 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2790 EX4672B-7300 Fundatie podului 5-225-culei 8 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2791 EX4672B-7300 Fundatie Culei 9 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2792 EX4672B-7300 Fundatie podului 5-225-culei 9 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2793 EX4672B-7300 Fundatie Culei 10 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2794 EX4672B-7300 Fundatie podului 5-225-culei 10 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2795 EX4672B-7300 Fundatie Culei 11 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2796 EX4672B-7300 Fundatie podului 5-225-culei 11 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2797 EX4672B-7300 Fundatie Culei 12 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2798 EX4672B-7300 Fundatie podului 5-225-culei 12 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2799 EX4672B-7300 Fundatie Culei 13 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2800 EX4672B-7300 Fundatie podului 5-225-culei 13 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2801 EX4672B-7300 Fundatie Culei 14 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2802 EX4672B-7300 Fundatie podului 5-225-culei 14 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2803 EX4672B-7300 Fundatie Culei 15 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2804 EX4672B-7300 Fundatie podului 5-225-culei 15 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2805 EX4672B-7300 Fundatie Culei 16 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2806 EX4672B-7300 Fundatie podului 5-225-culei 16 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2807 EX4672B-7300 Fundatie Culei 17 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2808 EX4672B-7300 Fundatie podului 5-225-culei 17 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2809 EX4672B-7300 Fundatie Culei 18 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2810 EX4672B-7300 Fundatie podului 5-225-culei 18 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2811 EX4672B-7300 Fundatie Culei 19 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2812 EX4672B-7300 Fundatie podului 5-225-culei 19 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2813 EX4672B-7300 Fundatie Culei 20 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2814 EX4672B-7300 Fundatie podului 5-225-culei 20 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2815 EX4672B-7300 Fundatie Culei 21 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2816 EX4672B-7300 Fundatie podului 5-225-culei 21 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2817 EX4672B-7300 Fundatie Culei 22 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2818 EX4672B-7300 Fundatie podului 5-225-culei 22 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2819 EX4672B-7300 Fundatie Culei 23 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2820 EX4672B-7300 Fundatie podului 5-225-culei 23 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2821 EX4672B-7300 Fundatie Culei 24 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2822 EX4672B-7300 Fundatie podului 5-225-culei 24 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2823 EX4672B-7300 Fundatie Culei 25 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2824 EX4672B-7300 Fundatie podului 5-225-culei 25 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2825 EX4672B-7300 Fundatie Culei 26 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2826 EX4672B-7300 Fundatie podului 5-225-culei 26 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2827 EX4672B-7300 Fundatie Culei 27 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2828 EX4672B-7300 Fundatie podului 5-225-culei 27 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2829 EX4672B-7300 Fundatie Culei 28 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2830 EX4672B-7300 Fundatie podului 5-225-culei 28 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2831 EX4672B-7300 Fundatie Culei 29 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2832 EX4672B-7300 Fundatie podului 5-225-culei 29 15-Sep-26 22-Sep-26 42 RONGUI RONGUI
- 2833 EX4672B-7300 Fundatie Culei 30 15-Sep-26 22-Sep-26 42 RONGUI RONGUI

[illegible]

Reab. Infr. rutiera DJ663, DJ672C,DJ672B,DJ665A, DJ664: actualizat la Februarie 2026 Update

CRITICAL_LAYOUT_FEB_2026

07-Mar-26 12:23

ID	Activity	Activity Name	Original Duration	Start	Finish	Actual	Complete	Status	Notes	2025												2026											
										Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
2567	█	EX-672B-2000 Fundulete balast		14-Jul-25	15-Jul-25		0%	-75	RONC000	RONC000																							
2567	█	EX-672B-2000 Piete Sparte -20cm dupa comp		2-Jul-25	20-Jul-25		0%	-75	RONC000	RONC000																							
2568	█	Podet 1m 10-172 Podet subteran instalat DN 1400 re		10-Jul-25	15-Jul-25		0%	-75	RONC000	RONC000																							
2569	█	EX-672B-1400 Montare montare la b.DF		2-Jul-25	15-Jul-25		0%	-75	RONC000	RONC000																							
2571	█	EX-672B-1400 Montare montare la b.DF		2-Jul-25	15-Jul-25		0%	-75	RONC000	RONC000																							
2572	█	EX-672B-1400 Fundulete podet		3-Jul-25	08-Jul-25		0%	-75	RONC000	RONC000																							
2573	█	EX-672B-1400 Realizare imprime camera de		2-Jul-25	15-Jul-25		0%	-75	RONC000	RONC000																							
2574	█	EX-672B-1400 Hidroizolatie podet		1-Jul-25	15-Jul-25		0%	-75	RONC000	RONC000																							
2575	█	Scara de Acces		4-Jul-25	10-Jul-25		0%	-30	RONC000	RONC000																							
2576	█	EX-672B-4400 Sandier param		4-Jul-25	10-Jul-25		0%	-30	RONC000	RONC000																							
2577	█	Scara de Acces		10-Jul-25	22-Jan-27		0%	-75	RONC000	RONC000																							
2578	█	EX-672B-1100 Freaza Autolapare 10-15cm		22-Jul-25	22-Jul-25		0%	-2	RONC000	RONC000																							
2579	█	EX-672B-1100 Freaza Autolapare 10-15cm		22-Jul-25	22-Jul-25		0%	-2	RONC000	RONC000																							
2580	█	EX-672B-1100 Scarific, repart si compact, fund		2-Jul-25	22-Jul-25		0%	-2	RONC000	RONC000																							
2581	█	EX-672B-1100 Oxidant curat aerifilant		5-Jul-25	08-Aug-25		0%	-2	RONC000	RONC000																							
2582	█	EX-672B-1140 Piete Sparte -20cm dupa comp		5-Jul-25	08-Aug-25		0%	-2	RONC000	RONC000																							
2583	█	EX-672B-1160 Annulare P.S. curentului		10-Aug-25	10-Aug-25		0%	-2	RONC000	RONC000																							
2584	█	EX-672B-1160 BAD 224 - 6 cm (inductiv)		04-Aug-25	10-Aug-25		0%	-2	RONC000	RONC000																							
2585	█	EX-672B-1180 Annulare BAD 224 curentu		5-Jul-25	20-Nov-25		0%	-60	RONC000	RONC000																							
2586	█	EX-672B-1180 BA 16 sau BAR 16 - 4 cm		5-Jul-25	20-Nov-25		0%	-60	RONC000	RONC000																							
2587	█	EX-672B-1170 BAD 224 - 1 cm (garnitur mediu)		11-Aug-25	20-Nov-25		0%	-2	RONC000	RONC000																							
2588	█	EX-672B-2200 Acostament Piete Sparte -10		14-Jul-27	15-Jul-27		0%	-75	RONC000	RONC000																							
2589	█	EX-672B-2200 Acostament Beton C 30/37 - 1		3-Jul-27	22-Jan-27		0%	-75	RONC000	RONC000																							
2590	█	Sector 6 km 10-300 km 1+1000 L+1500m Susaz		401 27-Aug-25A	15-Apr-27		0%	-10	RONC000	RONC000																							
2591	█	Sector 6 km 10-300 km 1+1000 L+1500m Susaz		401 27-Aug-25A	15-Apr-27		0%	-10	RONC000	RONC000																							
2592	█	Sector 6 km 10-300 km 1+1000 L+1500m Susaz		401 27-Aug-25A	15-Apr-27		0%	-10	RONC000	RONC000																							
2593	█	Lucrul Prelucrarea		3 27-Aug-25A	04-Mar-26		100%	-75	RONC000	RONC000																							
2594	█	EX-672B-2200 Picturare		3 27-Aug-25A	04-Mar-26		100%	-75	RONC000	RONC000																							
2595	█	EX-672B-2200 Curatare Defecti si scara de ind		3 27-Aug-25A	04-Mar-26		90%	-30	RONC000	RONC000																							
2596	█	EX-672B-2200 Taseare si scara de ind		3 27-Aug-25A	04-Mar-26		90%	-30	RONC000	RONC000																							
2597	█	Cantile Rutile		10 30-Jul-25	11-Aug-25		0%	-75	RONC000	RONC000																							
2598	█	EX-672B-2000 Sapatura		3 30-Jul-25	23-Jul-25		0%	-75	RONC000	RONC000																							
2599	█	EX-672B-2000 Stratificatie balast		3 30-Jul-25	23-Jul-25		0%	-75	RONC000	RONC000																							
2600	█	EX-672B-2000 Fundulete balast		2 30-Jul-25	23-Jul-25		0%	-75	RONC000	RONC000																							
3000	█	EX-672B-2000 Piete Sparte -20cm dupa comp		4 06-Aug-25	11-Aug-25		0%	-75	RONC000	RONC000																							
3001	█	Podet 1m 10-410 DN 800 - L+912m		12 30-Jul-25	05-Aug-25		0%	-75	RONC000	RONC000																							
3002	█	EX-672B-1400 Demontare podet instalat ind		10 30-Jul-25	03-Aug-25		0%	-75	RONC000	RONC000																							
3003	█	EX-672B-1400 Demontare podet instalat ind		22 30-Jul-25	22-Jul-25		0%	-75	RONC000	RONC000																							
3004	█	EX-672B-1000 Montare montare la b.DF		2 27-Jul-25	29-Jul-25		0%	-75	RONC000	RONC000																							
3005	█	EX-672B-1400 Fundulete podet		3 22-Jul-25	27-Jul-25		0%	-75	RONC000	RONC000																							
3006	█	EX-672B-1400 Realizare imprime bal		2 29-Jul-25	31-Jul-25		0%	-75	RONC000	RONC000																							
3007	█	EX-672B-1000 Hidroizolatie podet		1 19-Aug-25	09-Aug-25		0%	-75	RONC000	RONC000																							
3008	█	Podet 1m 10-410 DN 800 - L+912m		10 22-Jul-25	05-Aug-25		0%	-75	RONC000	RONC000																							
3009	█	EX-672B-1000 Demontare podet instalat ind		2 22-Jul-25	24-Jul-25		0%	-75	RONC000	RONC000																							
3010	█	EX-672B-1000 Realizare imprime camera de		2 29-Jul-25	31-Jul-25		0%	-75	RONC000	RONC000																							
3011	█	EX-672B-1000 Fundulete podet		3 24-Jul-25	24-Jul-25		0%	-75	RONC000	RONC000																							
3012	█	EX-672B-1000 Montare montare la b.DF		3 21-Jul-25	04-Aug-25		0%	-75	RONC000	RONC000																							
3013	█	EX-672B-1000 Hidroizolatie podet		1 04-Aug-25	05-Aug-25		0%	-75	RONC000	RONC000																							
3014	█	Podet 1m 10-410 DN 800 - L+1132m		12 30-Jul-25	05-Aug-25		0%	-75	RONC000	RONC000																							
3015	█	EX-672B-1000 Demontare podet instalat ind		2 20-Jul-25	20-Jul-25		0%	-75	RONC000	RONC000																							
3016	█	EX-672B-1000 Montare montare la b.DF		2 27-Jul-25	29-Jul-25		0%	-75	RONC000	RONC000																							
3017	█	EX-672B-1000 Fundulete podet		3 22-Jul-25	27-Jul-25		0%	-75	RONC000	RONC000																							
3018	█	EX-672B-1000 Montare montare la b.DF		3 21-Jul-25	04-Aug-25		0%	-75	RONC000	RONC000																							
3019	█	EX-672B-1000 Taseare balast		1 19-Aug-25	09-Aug-25		0%	-75	RONC000	RONC000																							
3020	█	EX-672B-1400 Hidroizolatie podet		1 04-Aug-25	05-Aug-25		0%	-75	RONC000	RONC000																							
3021	█	EX-672B-1000 Montare montare la b.DF		2 29-Jul-25	31-Jul-25		0%	-75	RONC000	RONC000																							
3022	█	Podet 1m 1160 DN 800 - L+912m		10 30-Jul-25	03-Aug-25		0%	-75	RONC000	RONC000																							

Reab. Infr. rutiera DJ663, DJ672C,DJ672B,DJ665A, DJ664: actualizat la Februarie 2026 Update

CRITICAL_LAYOUT_FEB_2026

07-Mar-26 12:23

#	Activity ID	Activity Name	Original Duration	Start	Finish	Activity % Complete	Total Prod.	Schedule Bar Cost	Actual Bar Cost	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
3072	EX-672B-1700	Montare si montare L&D DF	2	15-Aug-25	20-Aug-25	0%	-70	RON0.00	RON0.00																							
3073	EX-672B-1770	Fundatie podet	3	15-Aug-25	20-Aug-25	0%	-70	RON0.00	RON0.00																							
3074	EX-672B-1700	Realizare Impansibeton	2	20-Aug-25	20-Aug-25	0%	-70	RON0.00	RON0.00																							
3075	EX-672B-1800	Hidroizolare podet	1	24-Aug-25	25-Aug-25	0%	-70	RON0.00	RON0.00																							
3076	EX-672B-1900	Domeniu podet estelet induc	10	15-Aug-25	27-Aug-25	-72	RON0.00	RON0.00																								
3077	EX-672B-1900	Domeniu podet estelet induc	2	15-Aug-25	20-Aug-25	-72	RON0.00	RON0.00																								
3078	EX-672B-1900	Realizare Impansicamerele	2	20-Aug-25	24-Aug-25	0%	-72	RON0.00	RON0.00																							
3079	EX-672B-1900	Fundatie podet	3	17-Aug-25	20-Aug-25	0%	-72	RON0.00	RON0.00																							
3080	EX-672B-1940	Montare si montare Azpil /	2	24-Aug-25	26-Aug-25	0%	-72	RON0.00	RON0.00																							
3081	EX-672B-1900	Hidroizolare podet	1	15-Aug-25	20-Aug-25	0%	-72	RON0.00	RON0.00																							
3082	Podet km TH-HZ-DN 100-L=13.2m		12	15-Aug-25	27-Aug-25	-72	RON0.00	RON0.00																								
3083	EX-672B-1900	Domeniu podet estelet induc	2	11-Aug-25	13-Aug-25	0%	-72	RON0.00	RON0.00																							
3084	EX-672B-1900	Montare si montare clarene	2	18-Aug-25	20-Aug-25	0%	-72	RON0.00	RON0.00																							
3085	EX-672B-1900	Fundatie podet	3	15-Aug-25	20-Aug-25	0%	-72	RON0.00	RON0.00																							
3086	EX-672B-1900	Montare si montare Azpil /	2	24-Aug-25	26-Aug-25	0%	-72	RON0.00	RON0.00																							
3087	EX-672B-1910	Turarea beton de patla	1	24-Aug-25	25-Aug-25	0%	-71	RON0.00	RON0.00																							
3088	EX-672B-1900	Hidroizolare podet	1	18-Aug-25	27-Aug-25	0%	-72	RON0.00	RON0.00																							
3089	EX-672B-1900	Montare si montare clarene	2	15-Aug-25	20-Aug-25	0%	-72	RON0.00	RON0.00																							
3090	Podet km TH-HZ-DN 100-L=12.2m		10	11-Aug-25	25-Aug-25	-70	RON0.00	RON0.00																								
3091	EX-672B-1900	Domeniu podet estelet induc	2	11-Aug-25	13-Aug-25	0%	-75	RON0.00	RON0.00																							
3092	EX-672B-1900	Montare si montare L&D DF	2	18-Aug-25	20-Aug-25	0%	-70	RON0.00	RON0.00																							
3093	EX-672B-1900	Fundatie podet	3	15-Aug-25	20-Aug-25	0%	-75	RON0.00	RON0.00																							
3094	EX-672B-1900	Realizare Impansibeton	2	20-Aug-25	24-Aug-25	0%	-70	RON0.00	RON0.00																							
3095	EX-672B-1970	Hidroizolare podet	1	24-Aug-25	25-Aug-25	0%	-70	RON0.00	RON0.00																							
3096	Podet km TH-HZ-DN 1000-L=9.2m		2	18-Aug-25	01-Sep-25	-75	RON0.00	RON0.00																								
3097	EX-672B-1900	Domeniu podet estelet induc	2	18-Aug-25	20-Aug-25	0%	-75	RON0.00	RON0.00																							
3098	EX-672B-1900	Fundatie podet	3	20-Aug-25	23-Aug-25	0%	-75	RON0.00	RON0.00																							
3099	EX-672B-2010	Realizare Impansibeton	2	27-Aug-25	31-Aug-25	0%	-75	RON0.00	RON0.00																							
3100	EX-672B-2010	Hidroizolare podet	1	31-Aug-25	01-Sep-25	0%	-75	RON0.00	RON0.00																							
3101	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3102	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3103	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3104	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3105	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3106	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3107	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3108	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3109	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3110	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3111	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3112	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3113	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3114	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3115	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3116	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3117	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3118	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3119	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3120	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3121	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3122	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3123	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3124	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3125	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3126	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3127	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3128	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3129	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3130	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3131	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3132	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3133	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							
3134	EX-672B-2000	Montare si montare L&D DF	2	25-Aug-25	27-Aug-25	0%	-75	RON0.00	RON0.00																							

[illegible]

[illegible]

[illegible]

Reab. Infr. rutiera DJ663, DJ672C,DJ672B,DJ665A, DJ664: actualizat la Februarie 2026 Update										CRITICAL_LAYOUT_FEB_2026												07-Mar-26 12:23											
#	Activity	Activity Name	Original Duration	Start	Finish	Activity % Complete	Estimate	Actual Start	Actual End	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
3494	EX-672C-240	Montare si montare la DF	2	09-Jul-26	13-Jul-26	0%	19	RON-ND	RON-ND																								
3495	EX-672C-230	Fundatie podet	3	09-Jul-26	13-Jul-26	0%	19	RON-ND	RON-ND																								
3496	EX-672C-200	Realizare Impartibon	2	13-Jul-26	15-Jul-26	0%	19	RON-ND	RON-ND																								
3497	EX-672C-200	Hidroscap podet	1	15-Jul-26	16-Jul-26	0%	19	RON-ND	RON-ND																								
3498	Podet km 4+020 DN 100 - L=10.2m		10	30-Jul-26	14-Jul-26	0%	21	RON-ND	RON-ND																								
3499	EX-672C-210	Demontare podet existent inclu	2	30-Jul-26	03-Aug-26	0%	19	RON-ND	RON-ND																								
3500	EX-672C-200	Montare si montare la DF	2	07-Jul-26	09-Jul-26	0%	21	RON-ND	RON-ND																								
3501	EX-672C-200	Fundatie podet	3	03-Jul-26	07-Jul-26	0%	21	RON-ND	RON-ND																								
3502	EX-672C-210	Realizare Impartibon	2	09-Jul-26	13-Jul-26	0%	21	RON-ND	RON-ND																								
3503	EX-672C-210	Hidroscap podet	1	13-Jul-26	15-Jul-26	0%	21	RON-ND	RON-ND																								
3504	Podet km 4+020 DN 100 - L=11.5m		10	03-Jul-26	16-Jul-26	0%	19	RON-ND	RON-ND																								
3505	EX-672C-210	Demontare podet existent inclu	2	03-Jul-26	09-Jul-26	0%	19	RON-ND	RON-ND																								
3506	EX-672C-210	Montare si montare la DF	2	09-Jul-26	13-Jul-26	0%	19	RON-ND	RON-ND																								
3507	EX-672C-210	Fundatie podet	3	09-Jul-26	13-Jul-26	0%	19	RON-ND	RON-ND																								
3508	EX-672C-210	Realizare Impartibon	2	13-Jul-26	15-Jul-26	0%	19	RON-ND	RON-ND																								
3509	EX-672C-210	Hidroscap podet	1	15-Jul-26	16-Jul-26	0%	19	RON-ND	RON-ND																								
3510	Podet km 4+020 DN 100 - L=11.5m		10	30-Jul-26	14-Jul-26	0%	21	RON-ND	RON-ND																								
3511	EX-672C-210	Demontare podet existent inclu	2	30-Jul-26	03-Aug-26	0%	19	RON-ND	RON-ND																								
3512	EX-672C-210	Montare si montare la DF	2	07-Jul-26	09-Jul-26	0%	21	RON-ND	RON-ND																								
3513	EX-672C-210	Fundatie podet	3	03-Jul-26	07-Jul-26	0%	21	RON-ND	RON-ND																								
3514	EX-672C-210	Realizare Impartibon	2	09-Jul-26	13-Jul-26	0%	21	RON-ND	RON-ND																								
3515	EX-672C-210	Hidroscap podet	1	13-Jul-26	15-Jul-26	0%	21	RON-ND	RON-ND																								
3516	Podet km 4+020 DN 100 - L=10.2m		10	03-Jul-26	16-Jul-26	0%	19	RON-ND	RON-ND																								
3517	EX-672C-220	Demontare podet existent inclu	2	03-Jul-26	09-Jul-26	0%	19	RON-ND	RON-ND																								
3518	EX-672C-240	Montare si montare la DF	2	09-Jul-26	13-Jul-26	0%	19	RON-ND	RON-ND																								
3519	EX-672C-220	Fundatie podet	3	09-Jul-26	13-Jul-26	0%	19	RON-ND	RON-ND																								
3520	EX-672C-220	Realizare Impartibon	2	13-Jul-26	15-Jul-26	0%	19	RON-ND	RON-ND																								
3521	EX-672C-220	Hidroscap podet	1	15-Jul-26	16-Jul-26	0%	19	RON-ND	RON-ND																								
3522	Trotuar		6	14-Sep-26	22-Sep-26	0%	44	RON-ND	RON-ND																								
3523	EX-672C-430	Decoprire /scapare	1	14-Sep-26	15-Sep-26	0%	44	RON-ND	RON-ND																								
3524	EX-672C-430	Montare /Bordura /10x50cm	2	15-Sep-26	17-Sep-26	0%	44	RON-ND	RON-ND																								
3525	EX-672C-430	Fundatie balast -15cm, dupa	1	17-Sep-26	18-Sep-26	0%	44	RON-ND	RON-ND																								
3526	EX-672C-430	Dale beton C 1600 - 10cm	1	18-Sep-26	21-Sep-26	0%	44	RON-ND	RON-ND																								
3527	EX-672C-430	Beton variat B4-4 cm	1	21-Sep-26	22-Sep-26	0%	44	RON-ND	RON-ND																								
3528	Stali Autobuz		10	08-Dec-26	11-Dec-26	0%	39	RON-ND	RON-ND																								
3529	EX-672C-470	Sapetia	2	09-Dec-26	10-Dec-26	0%	39	RON-ND	RON-ND																								
3530	EX-672C-470	Stratofornie tip - 7cm, dupa	2	10-Dec-26	11-Dec-26	0%	39	RON-ND	RON-ND																								
3531	EX-672C-470	Fundatie balast -30cm, dupa	2	10-Dec-26	14-Dec-26	0%	39	RON-ND	RON-ND																								
3532	EX-672C-470	Pista Sports -20cm, dupa	2	11-Dec-26	11-Dec-26	0%	39	RON-ND	RON-ND																								
3533	EX-672C-470	BAD 224 - 6cm (inclusiv strat)	2	14-Dec-26	16-Dec-26	0%	39	RON-ND	RON-ND																								
3534	EX-672C-470	Amorsare PS -BAD 224 cu	2	14-Dec-26	16-Dec-26	0%	39	RON-ND	RON-ND																								
3535	EX-672C-470	BA 16cm/BAD 16 -4cm	2	16-Dec-26	16-Dec-26	0%	39	RON-ND	RON-ND																								
3536	EX-672C-470	Adaptare pentru scapare	2	16-Dec-26	16-Dec-26	0%	39	RON-ND	RON-ND																								
3537	Scapare/Apeler		19	12-Nov-26	10-Dec-26	0%	23	RON-ND	RON-ND																								
3538	EX-672C-580	Regla comestibila D=8 cm +	2	12-Nov-26	13-Nov-26	0%	23	RON-ND	RON-ND																								
3539	EX-672C-570	Sart-pier (fina scapare)	17	16-Nov-26	10-Dec-26	0%	23	RON-ND	RON-ND																								
3540	Acces la Proiect		4	14-Jul-26	16-Sep-26	0%	35	RON-ND	RON-ND																								
3541	EX-672C-560	Podet acces la proiect	34	20-Jul-26	04-Sep-26	0%	30	RON-ND	RON-ND																								
3542	EX-672C-580	Sapetia	10	28-Jul-26	11-Aug-26	0%	52	RON-ND	RON-ND																								
3543	EX-672C-560	Fundatie balast -30cm, dupa	10	21-Aug-26	0																												

■ Activities ■ Remaining Work ▶ Summary
■ Actual Work ◆ Milestone

Page 35 of 36

TASK filter: All Activities

© Oracle Corporation

